Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Scenario: Community Lost & Found Matching Network | Jira project: SE lab 2 (key SL2)

Samarth Prabhu K | SRN PES1UG24CS905

1. Epics

The Lab 1 functional requirements were grouped into five functional themes, one epic each. The backlog holds 5 epics and 10 user stories, totalling 63 story points.

Key	Epic	Lab 1 source	Priority	Stories	Points
SL2-1	Lost & Found Reporting	FR002, UC-01, UC-02	High	SL2-6, SL2-7	10
SL2-2	Item Tag Extraction	FR003	Medium	SL2-8	8
SL2-3	Lost–Found Matching	FR001, NFR002, UC-03	High	SL2-9, SL2-12	21
SL2-10	Match Notifications	FR004	Medium	SL2-13	5
SL2-11	Ownership Verification & Claim	FR005, NFR001, UC-04/04a	High	SL2-15, SL2-16, SL2-17, SL2-18	19

2. User stories, priorities and story points

Key	User story (As a… I want… so that…)	Epic	Priority	Pts	Sprint
SL2-9	As a potential owner, I want Lost Item reports matched with compatible Found Item reports by category, colour tags and location radius, so that I can identify a possible match.	SL2-3	Highest	13	1
SL2-6	As a Finder/Owner, I want to create and submit a Lost Item report with item details, location and visual/text information, so that the system can use it for matching.	SL2-1	High	5	1
SL2-7	As a Finder/Owner, I want to create and submit a Found Item report with item details, location and visual/text information, so that it is available for matching.	SL2-1	High	5	1
SL2-8	As a Finder/Owner, I want the system to extract visual and text item tags from my report, so that the right attributes are associated for matching.	SL2-2	Medium	8	1
SL2-12	As a potential owner, I want the system to record a match probability, so that I can assess how likely the match is to be my item.	SL2-3	Medium	8	1
SL2-15	As a claimant, I want to answer the Finder's private security questions, so that I can prove ownership of the found item.	SL2-11	High	5	2
SL2-16	As the system, I want to validate the claimant's security-question answers, so that ownership is verified before contact details are revealed.	SL2-11	High	8	2
SL2-17	As a verified claimant, I want the permitted handover contact details revealed after successful verification, so that I can arrange the handover.	SL2-11	High	3	2
SL2-18	As the system, I want to keep handover contact details hidden when answers are incorrect, so that unauthorized claims are prevented.	SL2-11	High	3	2
SL2-13	As a potential owner, I want a notification when my Lost Item report receives a qualifying match, so that I can act on it.	SL2-10	Medium	5	2

Prioritization rule. Priorities follow the Lab 1 requirement priorities, ranked by user impact: matching (FR001) is the core value of the system, so SL2-9 is Highest. Reporting (FR002) and secure claiming (FR005, NFR001) are High because without reports nothing can be matched, and without verification a match cannot safely end in a handover. Tag extraction (FR003), match probability, and notifications (FR004) are Medium: they improve matching and response time, but the core loop works without them.

Estimation. Story points use the Fibonacci scale (1, 2, 3, 5, 8, 13…), sized by planning poker. Each member picks a card privately, all cards are revealed together, and the highest and lowest voters explain their reasoning before a re-vote. Gaps widen with size because uncertainty grows with size: 13 for matching reflects the unknowns in


combining category, colour, and radius into one score, while 3 for revealing contact details is a simple gated read. SL2-7 was first estimated at 4, which is not a Fibonacci value. It was re-estimated to 5 to match its twin story SL2-6.

3. Sprint plan and outcome


Sprint	Duration	Goal	Stories	Committed	Completed
SL2 Sprint 1	1 week (28 Aug – 4 Sep 2026)	A reported item can be tagged and matched against reports of the other type.	SL2-6, 7, 8, 9, 12	38 pts*	38 pts
SL2 Sprint 2	1 week (28 Aug – 4 Sep 2026)	A matched owner is notified and can securely verify ownership to obtain handover contact.	SL2-13, 15, 16, 17, 18	24 pts	24 pts

* Sprint 1 was committed at 38 points, while SL2-7 was still estimated at 4. After the re-estimate the story total is 39. Jira's reports keep the commitment as it stood at sprint start.


4. Jira screenshots

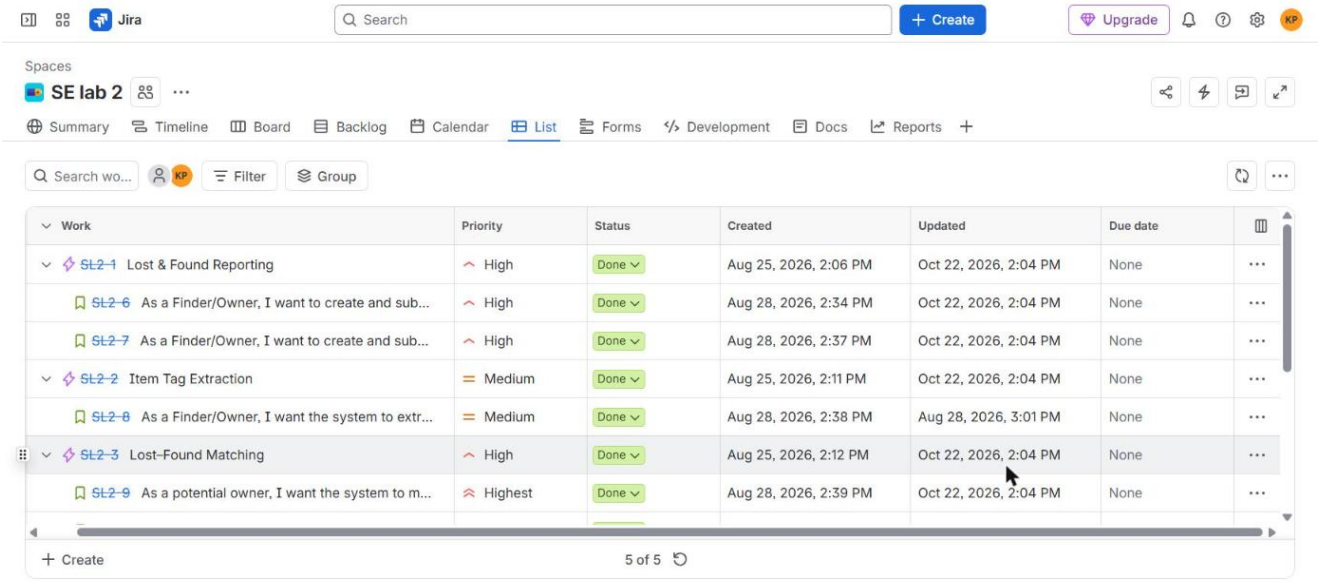


Backlog (List view): epics with their child user stories and priorities — part 1

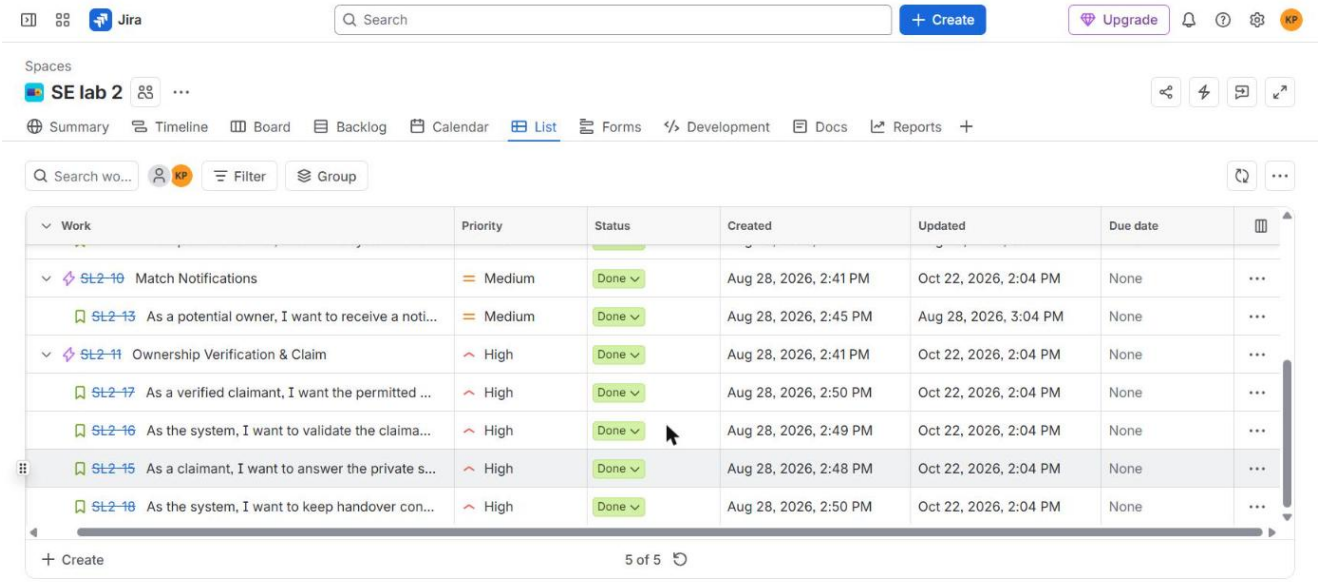


Backlog (List view): epics with their child user stories and priorities — part 2

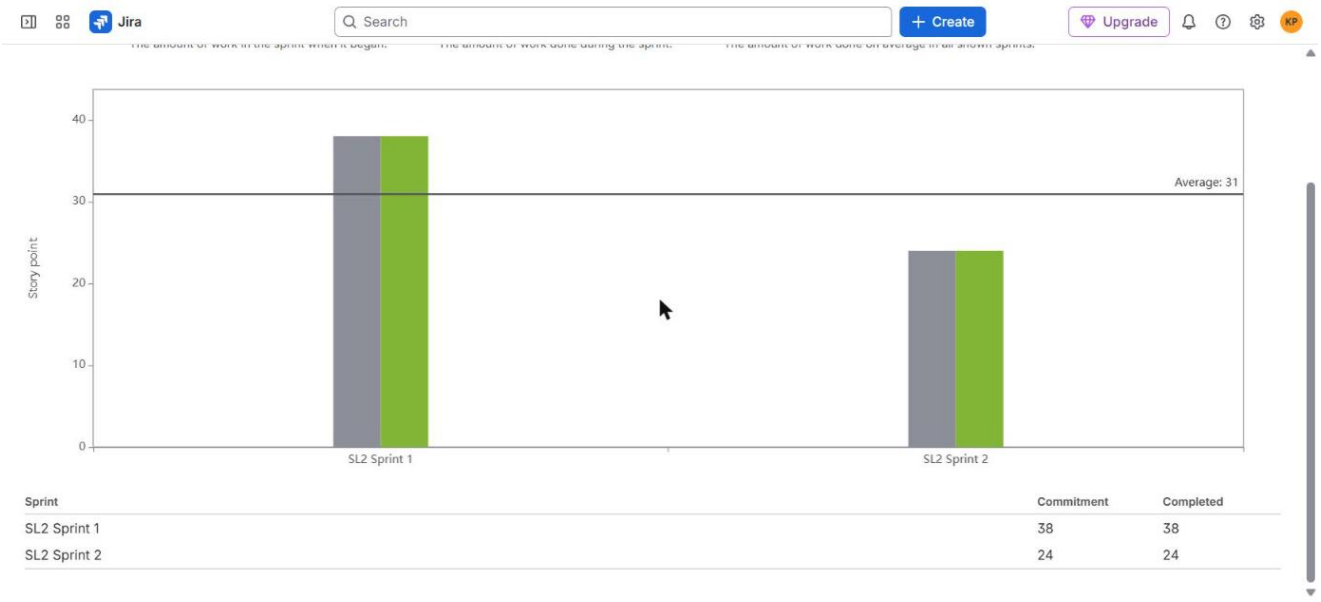

Story points per sprint: commitment vs completed (Velocity report), average 31 points

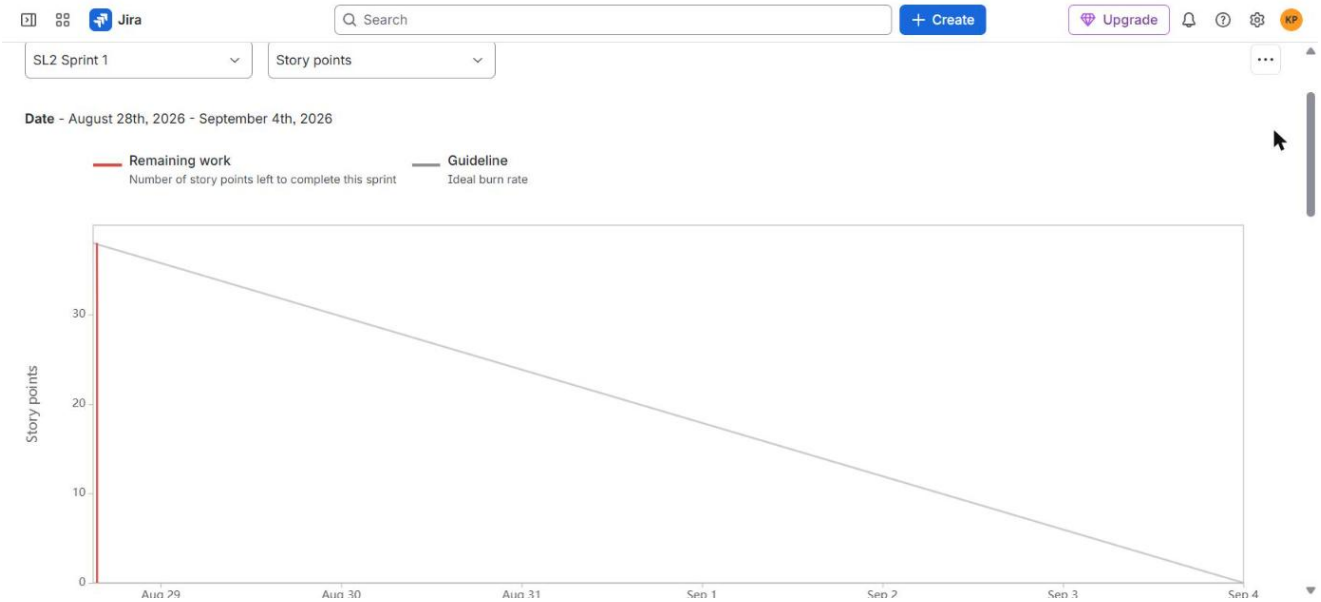

Burndown chart — SL2 Sprint 1 (38 story points)

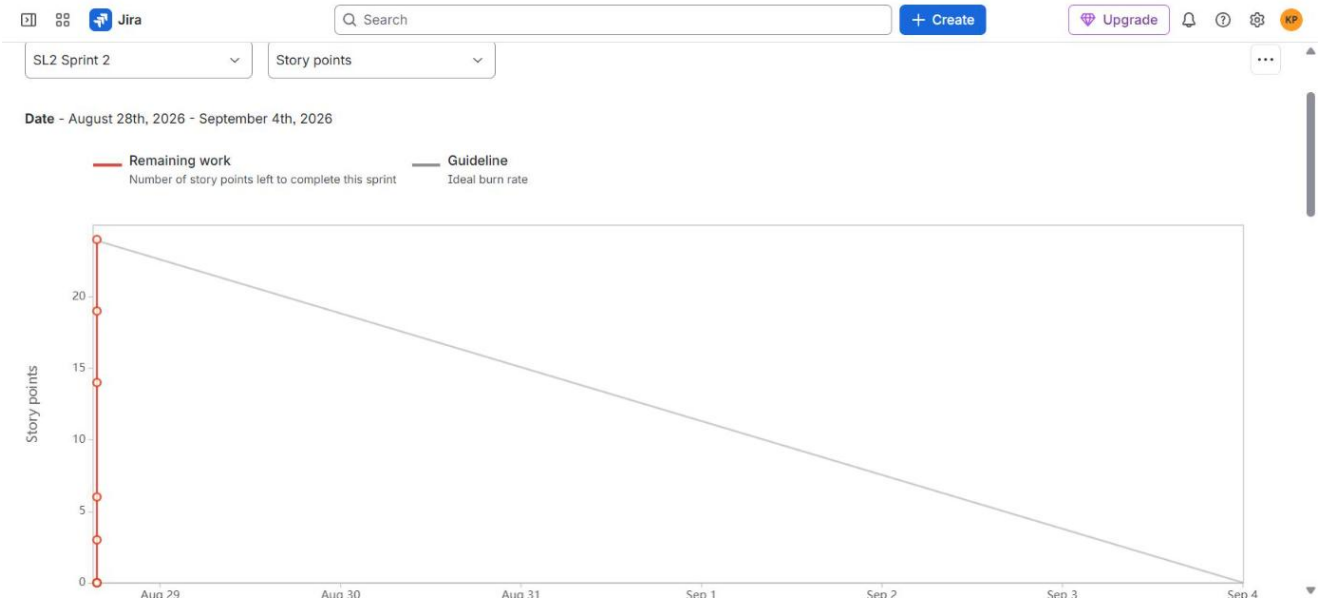

Burndown chart — SL2 Sprint 2 (24 story points)

5. Reflection questions

1. Did your estimations reflect the actual effort?

As relative sizes, yes. Matching (13) and answer validation (8) are clearly the most complex stories, and revealing or hiding contact details (3 each) are simple conditional reads. As effort predictions they could not be tested: the sprint was simulated, so every story was moved to Done within minutes regardless of its size. The useful outcome was catching an estimation error. SL2-7 was given 4 points, a value outside the Fibonacci scale, and was corrected to 5.

2. Was your backlog well-prioritized?

Mostly. Sprint 1 took everything that matching depends on (reports, tags, the match engine and its probability), and Sprint 2 took everything that depends on a match existing (notification, verification, handover). So no story was planned before something it depends on. One weakness: SL2-12 (match probability) is Medium yet sat in Sprint 1, while High verification stories waited for Sprint 2. Priority alone would have ordered them differently. Dependencies, not just priority, decided the sprint split.

3. How did your simulated sprint align with your plan?

Both sprints delivered 100% of their commitment: 38/38 points in Sprint 1 and 24/24 in Sprint 2, with no work carried over. The deviation was in timing, not scope. Each sprint was planned for one week, but all stories were completed on 28 Aug, the first day. So the plan's assumption of work spread across the week was never exercised.

4. What insights did the burndown chart give about your team's capacity?

In both charts the red remaining-work line drops vertically to zero at the start of the sprint, far below the grey guideline. Read literally, the team finished early and under-committed. Here, though, the shape is an artifact of simulating the sprint in minutes. A single steep drop is also the pattern the handout warns about: work completed in one batch instead of incrementally. The real capacity signal is velocity. Completed points were 38 and 24, an average of about 31 points per one-week sprint. That is the figure to use when sizing Sprint 3.
